

Instructions

Getting Started

Only the yellow-highlighted cells on the Job Data sheet are for data entry. Every white cell with black text is a formula; leave it alone. WIP Schedule and Closed Jobs sheets are read-only views — they update automatically based on each job's status (0, 1, 2) in column AH; never manually enter data, edit, or delete rows on those two sheets. Any changes to a job — opening, closing, archiving, or clearing it — are made on the Job Data sheet.

Status (col AG): 1 = Open (shows on WIP Schedule), 2 = Closed (moves to Closed Jobs), 0 = Archived (removes job from WIP Schedule or Closed Jobs sheet without deleting data; fully reversible by retyping a 1 or 2 in column AH).

Award Date and Date Closed control sorting: the most recent date appears at the top of WIP Schedule and Closed Jobs. If two jobs share the same date, whichever was entered first appears first.

Once the accounting period has closed, it's safe to permanently clear any completed (closed) jobs from this workbook. To do so, change the Status in column AH from 2 to 0 — this removes the entry from the Closed Jobs sheet. Next, click the corresponding row number on the left side of the sheet to select the entire row, right-click anywhere on the selected row, and choose "Clear Contents" from the menu. DO NOT DELETE ROWS. If a row is inadvertently deleted, press Ctrl+Z (Cmd+Z on Mac) immediately, before making any other changes or saving, and it will be fully restored.

Once a job is cleared on this sheet and the workbook is closed, Undo can no longer bring it back — restore it from a previously saved copy (if one exists) or re-enter the data.

Column Notes

Estimate Section (cols C–H)

Original Contract Value (col C) and Approved Change Orders (col D) are manual inputs; Total Contract Revenue (col E) is their sum, calculated automatically.

Total Contract Costs (col F) = Direct Costs To Date (col AE) + Estimated Costs to Complete (col AF). This is a living, continuously-updated estimate — not your original bid — matching standard percentage-of-completion practice under ASC 606. Update Estimated Costs to Complete (col AF) each period as field conditions change; your original budget number lives only in your accounting system, since this WIP tracks progress, not bid variance.

Gross Profit (Loss) (col G) and Gross Profit % (col H) are the budget-level margin — Total Contract Revenue minus Total Contract Costs, and that profit as a percentage of revenue. Both recalculate automatically as Total Contract Costs moves.

Job to Date Section (cols I–O)

% Complete (col I) = Direct Costs To Date (col AE) ÷ Total Contract Costs (col F) — the standard cost-to-cost method.

Earned Contract Revenue To Date (col J) = Total Contract Revenue × % Complete. Direct Costs To Date (col K) is a duplicate of column AE, shown here for convenience so you don't have to scroll to the Cost section to see it alongside % Complete and Earned Revenue. Gross Profit (Loss) To Date (col L) = Earned Revenue To Date minus Direct Costs To Date — calculated by subtraction, in that order. (An earlier version of this workbook computed Earned Revenue from Gross Profit instead, which was circular — Gross Profit can't be an input to the very figure it's derived from. This version fixes that.)

Gross Profit — Prior Year (col M) is a manual input — a frozen snapshot of cumulative gross profit as of the end of your last fiscal year, locked once your books close and taxes are filed for that year. Gross Profit — Current Period (col N) = Gross Profit (Loss) To Date minus Gross Profit — Prior Year, i.e. everything earned this fiscal year alone. Gross Profit Current Period % (col O) is that current-period profit as a percentage of this period's cost-plus-profit basis — useful for spotting a job whose profitability is trending up or down this year, separate from its all-time cumulative picture.

Job to Date Billings Section (cols P–S)

Contract Billings To Date (col P) is a manual input — your cumulative billings on this job, all-time. Prior Year Billings (col Q) is a manual input — a frozen snapshot of cumulative billings as of your last fiscal year-end, the same annual-lock convention as Gross Profit — Prior Year.

Under/(Over) Billings (col R) = Earned Contract Revenue To Date minus Contract Billings To Date (positive = underbilled, negative = overbilled). Prior Year Under/(Over) Billing (col S) applies the identical formula using only the prior-year figures (Prior Year Direct Costs + Gross Profit — Prior Year, minus Prior Year Billings) — letting you compare whether your billing position is improving or worsening year over year, not just where it stands today.

Cost Section (cols U–AF)

Labor (col U), Materials (col V), Subs (col W), Equipment (col X), and Other (col Y) are manual inputs representing THIS FISCAL YEAR's activity only — not lifetime-to-date. This figure must reflect direct labor burden — payroll taxes, workers' comp, benefits, etc. — not just base wages.

Allocated Labor Costs (col Z), Indirect Equipment Costs (col AA), and Other Indirect Allocation Costs (col AB) are manual inputs, also current-fiscal-year-only. Most small-business accounting programs (QuickBooks and similar) do not automatically allocate these costs to jobs the way a dedicated construction ERP would — you'll need to calculate the amounts outside this workbook (many payroll systems make labor burden easier to compute via a report like a payroll summary) and enter the totals here manually.

Total Current Costs (col AC) sums all eight cost categories above — calculated automatically, not an input.

Prior Year Direct Costs (col AD) is a manual input — a frozen lump-sum snapshot of everything this job cost before this fiscal year, locked once your books close and taxes are filed. Direct Costs To Date (col AE) = Total Current Costs + Prior Year Direct Costs — the true lifetime-to-date figure, calculated automatically. This is the same value duplicated at col J in the Job to Date section above.

Estimated Costs to Complete (col AF) is a manual input — your best current estimate of remaining cost to finish this job, updated every period as field conditions change. This feeds Total Contract Costs (col F) directly, so keeping it current is what keeps % Complete and Gross Profit accurate.


Reporting Frequency & Bundled-Elsewhere Toggles (rows 3–4)

Job Cost & Billing Snapshot


Closed jobs are on the Closed Jobs tab.

Total Contract Revenue	Direct Costs To Date	Gross Profit (Budget)	Net Over/(Under) Billing	Remaining Backlog Revenue (Open Jobs)	Remaining Backlog Margin (Open Jobs)
\$4,118,427	\$1,987,742	\$888,775	\$312,982	\$1,586,163	\$344,253


Earned Revenue vs. Billed — Active Jobs

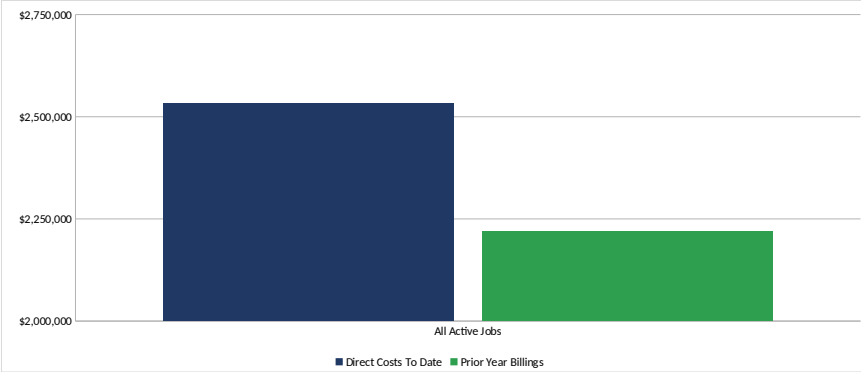


Backlog by Job — Revenue vs. Cost (Top 5 + Other)

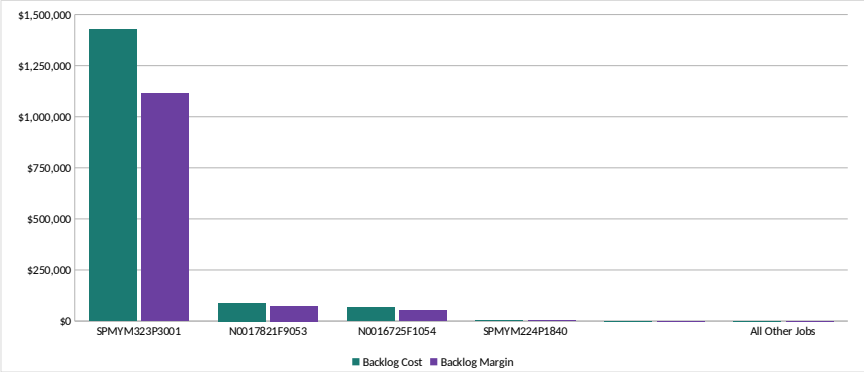

Contract Costs: Budget vs. Actual — Active Jobs

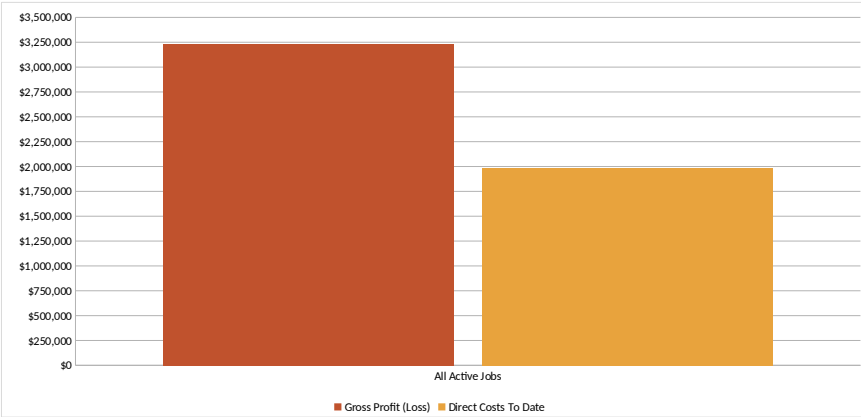

Contract Revenue Concentration — Active Jobs (Top 5 + Other)

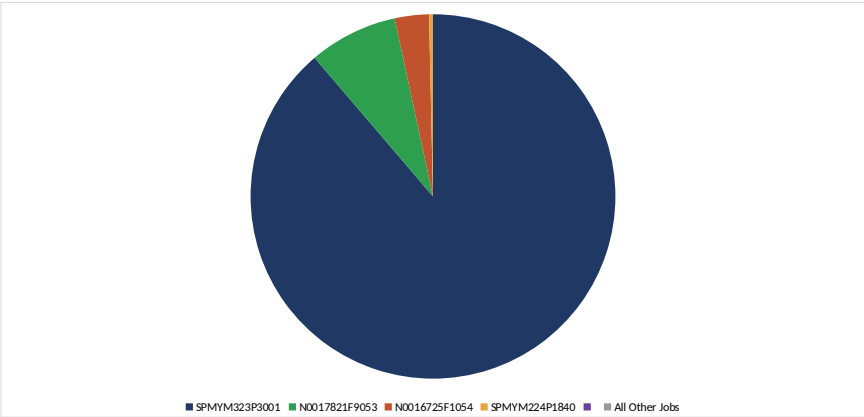

Billing Status — Active Jobs

0 of 4 jobs on track

Billing Status	# of Jobs	Total \$
Overbilled	0	\$0
Underbilled	4	\$312,982
Difference (Net Position)		(\$312,982)

Only the yellow-highlighted cells on this sheet are for data entry. Every white cell with black text is a formula; leave it alone. Never manually edit WIP Schedule or Closed Jobs — all job management happens here, driven by Status (col AH). See the Instructions tab for full details on Status codes, date sorting, column definitions, and how to safely clear a worksheet.

[illegible]

Auto-populated from the Job Data tab — Flagged Status = 1 (Open). Once a job's Status is changed to 2 (Closed) on the Job Data sheet, it moves to Closed Jobs automatically.

No manual entry or copy/pasting required.

Job ID #	Description	Preproduction			Bidding										Cost To Date and Estimated Cost To Complete										Backlog								
		Original Contract Value	Approved Change Orders	Total Contract Revenue	Total Contract Costs	Gross Profit (L) to Date	Gross Profit % To Date	Current Contract Revenue To Date	Gross Profit To Date	Gross Profit (L) to Date	Gross Profit % To Date	Gross Profit - Prior Year	Gross Profit - Current Period	Contract Margin To Date	Year To Date Revenue (Bidding)	Year To Date Revenue (Bidding)	Bidding Flag	Labor	Materials	Subs	Equipment	Other	Allocated Labor Costs	Indirect Equipment Costs	Other Indirect Allocation Costs	Total Current Costs	Prior Year Gross Costs	Current Costs To Date	Estimated Costs To Complete	Backlog Revenue	Backlog Cost	Backlog Margin	Backlog Margin %
10001-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10002-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10003-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10004-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10005-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10006-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10007-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10008-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10009-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10010-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10011-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10012-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10013-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10014-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10015-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10016-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10017-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10018-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10019-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10020-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10021-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10022-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10023-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10024-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10025-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10026-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10027-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10028-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10029-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10030-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
10031-100-1000	CLD Prod Assembly - Transport Package (SAMPLE)	\$100,000.00	\$0.00	\$100,000.00	\$80,000.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	20.00%	\$0.00	\$20,000.00	20.00%	\$100,000.00	\$20,000.00	\$100,000.00	Completed	\$1,000.00	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%

Closed Jobs — Contracts Completed

Auto-populated from the Job Data tab — flagged Status = 2 (Closed). No manual entry or copying/pasting required.

Search:																																	
Job / PO #	Description	Original Contract Value	Approved Change Orders	Total Contract Revenue	Total Contract Costs	Gross Profit (Loss)	Gross Profit %	% Complete	Earned Contract Revenue To Date	Direct Costs To Date	Gross Profit (Loss) To Date	Gross Profit Year - Prior Year	Gross Profit - Current Period	Gross Profit Current Period %	Contract Billings To Date	Prior Year Billings	Under(Over) Billings	Prior Year Under(Over) Billing	Labor	Materials	Subs	Equipment	Other	Allocated Labor Costs	Indirect Equipment Costs	Other Indirect Allocation Costs	Total Current Costs	Prior Year Direct Costs	Direct Costs To Date	Estimated Costs To Complete	PM Initials		
SPMYM23P1318	Weight Test 20000 (SAMPLE)	\$944,876.00	\$0.00	\$944,876.00	\$325,000.00	\$619,876.00	65.6%	100.0%	\$944,876.00	\$325,000.00	\$619,876.00	\$100,174.96	\$519,704.04	56.7%	\$944,876.00	\$944,876.00	\$0.00	(\$122,444.06)	\$119,171.00	\$159,041.00	\$19,863.00	\$19,863.00	\$39,726.00	\$0.00	\$11,917.80	\$47,871.20	\$397,360.00	\$722,260.00	\$325,000.00	\$0.00			
SPMYM23P4828	Plutonium (SAMPLE)	\$23,888.00	\$0.00	\$23,888.00	\$0.00	\$23,888.00	100.0%	100.0%	\$23,888.00	\$0.00	\$23,888.00	\$0.00	\$23,888.00	56.4%	\$23,888.00	\$23,888.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
ND016723P112	CLB ADD CTR Future (SAMPLE)	\$149,322.50	\$0.00	\$149,322.50	\$0.00	\$149,322.50	86.0%	100.0%	\$149,322.50	\$0.00	\$149,322.50	\$119,012.70	\$30,309.80	55.0%	\$149,322.50	\$149,322.50	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	
SPMYM23P0907	Ladder Tread (SAMPLE)	\$5,300.00	\$0.00	\$5,300.00	\$0.00	\$5,300.00	100.0%	100.0%	\$5,300.00	\$0.00	\$5,300.00	\$0.00	\$5,300.00	56.9%	\$5,300.00	\$5,300.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	
ND016723P192	BSS OTR Shipping Future (SAMPLE)	\$249,698.00	\$0.00	\$249,698.00	\$93,485.00	\$156,213.00	62.6%	100.0%	\$249,698.00	\$93,485.00	\$156,213.00	\$31,364.00	\$124,849.00	57.2%	\$249,698.00	\$249,698.00	\$0.00	(\$31,243.00)	\$32,719.75	\$32,719.75	\$4,714.25	\$9,348.50	\$4,714.25	\$9,348.50	\$0.00	\$11,218.20	\$93,485.00	\$186,970.00	\$93,485.00	\$0.00			
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		
\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	0.0%	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.0%	\$0.00	\$0.00	\$0.00	\$															
